




INNER WEST COUNCIL

Ashfield Town Centre Upgrade

Construction Update October 2017

Construction of the \$7 M Ashfield Town Centre Upgrade commenced in June 2017. Works are progressing on schedule and are set to deliver substantial benefits to residents and local businesses.

Construction of the upgrade is being carried out in accordance with the staging plan below.

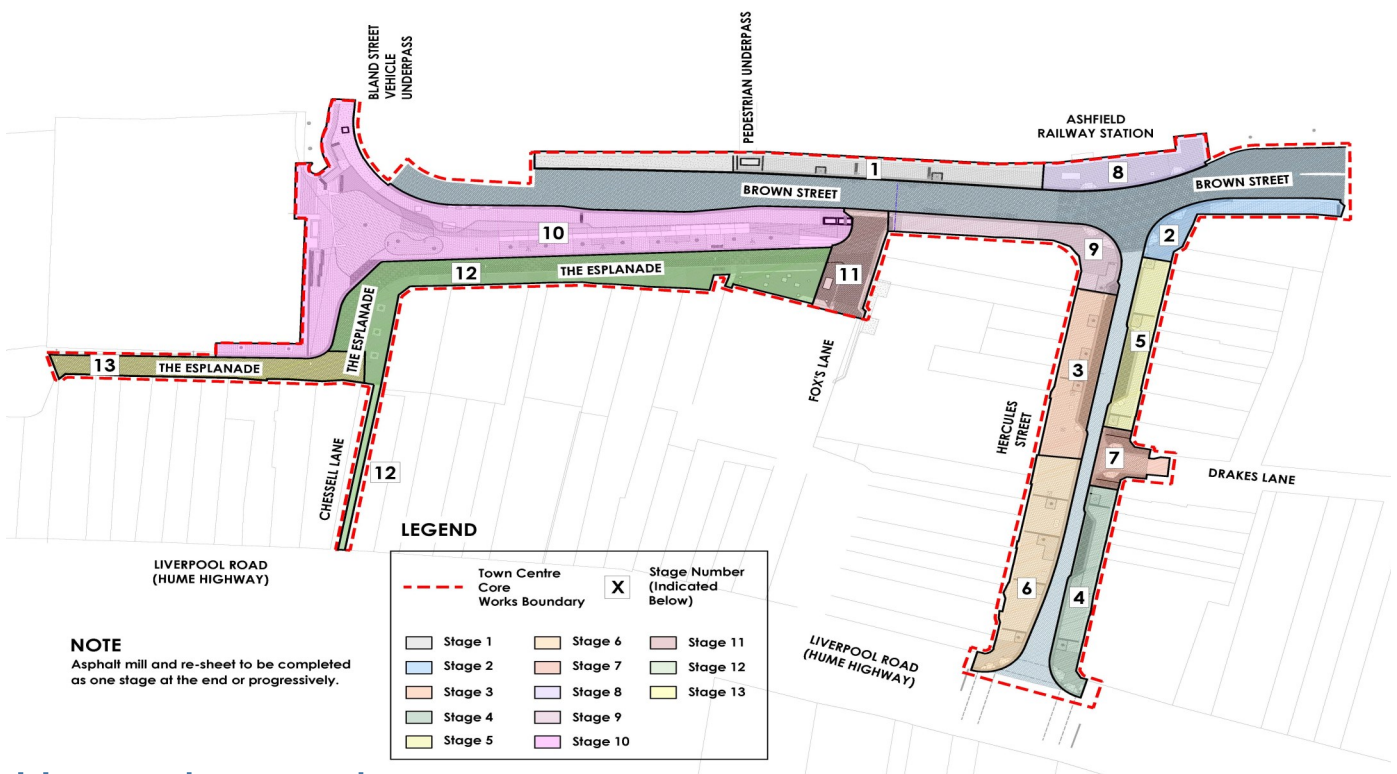

Upcoming works

Work has commenced on Stage 10 - Brown Street. The bus stop has been temporarily relocated between Hercules Street and the 2A Brown Street carpark, and the footpath is temporarily closed.

Construction will then proceed with the demolition and re-construction of the retaining wall.

When will the project be completed?

Works on Hercules Street and the retail areas are scheduled to be finalised by December 2017. The overall project is expected to be completed by May 2018, weather permitting.

Progress To Date

The status of each stage of construction is as follows:

Stage	Status
Stage 1 - Brown St	Substantially completed.
Stage 2 - Brown St	Substantially completed. New timber pole to be installed on the corner for Ausgrid.
Stage 5 - Hercules St	Substantially completed. Some works remain such as the relocation of Optus cables, removal of timber poles, landscaping and some paving around the tree pits.
Stage 3 - Hercules St	Demolition and the majority of concrete works have been completed. Paving has commenced and this stage is expected to be substantially complete by mid October.
Stage 4 - Hercules St	Demolition and the majority of concrete works have been completed. Paving has commenced and this stage is expected to be substantially complete by the end of October.
Electrical Works	Trenching and laying of conduits is progressing along The Esplanade and Markham Place. This work will enable the power to be undergrounded, the old timber poles to be removed and new lighting installed.

How to get more information

Council will continue to regularly update residents and businesses on progress of the works.

Council's contractor for the works, CA&I Pty Ltd, has appointed a community liaison officer to be available at all times. His contact details are listed below.

If you need further information about the upgrade please contact Inner West Council.

If English is not your first language please email Council at council@innerwest.nsw.gov.au or call 9392 5000.

如果英语不是您的第一种语言，请给委员会发电子邮件到 council@innerwest.nsw.gov.au 或致电

Inner West Council
260 Liverpool Road Ashfield NSW 2131
PO Box 1145 Ashfield NSW 1800
Tel (02) 9392 5000
council@innerwest.nsw.gov.au
www.innerwest.nsw.gov.au

CA&I Pty Ltd
Community Liaison Officer: Menios Mitakidis
Phone 0404 090 147
menios_mitakidis@ca-i.com.au
www.ca-i.com.au
